

VALDEZ MIDDLE SCHOOL

CONSTRUCTION PHOTO REPORT No. 14- 10

MARCH 10, 2014 –MARCH 16, 2014


KEY CONSTRUCTION ACTIVITIES

Dawson staged, inventoried and started installing metal siding and flashing along north and east sides of building. Inside, Dawson installed plywood on walls for Gym storage, installed sleeves in Gym floor for volleyball and badminton posts, adjusted door frames, performed other miscellaneous rough carpentry and layout. Megawatt continued work on main panels in Electrical room, terminated panel boards in Admin area, pulled control wire to VAVs, and started installing fixtures in Gym and hard ceilings. Integrity continued installing J-hooks and pulled data cable for classrooms. Mantech unloaded and set boilers in the mechanical room, continued work on heat mains and started connecting pipe to hot water generators. H&H Sheetmetal installed dust collector drops in CTE ducts, connected supply and exhaust ducts, and connected exhaust stacks to boilers. All Wall hung sheetrock on walls at the Cafeteria, Kitchen, Shipping and Receiving and Special Education, various ceilings and soffits, installed sound insulation and caulking; finished taping and sanding Gym and classrooms; finished painting Admin area, continued painting the Gym and started painting classrooms. Alaska Glazing installed the curtain wall frame and half the glazing at the entry.



Installing horizontal metal panel (MP-2) siding on hat channel along east wall of Gym (left) and north wall of Mat room.

**VALDEZ MIDDLE SCHOOL
CONSTRUCTION PHOTO REPORT No. 14- 10
MARCH 10, 2014 -MARCH 16, 2014**

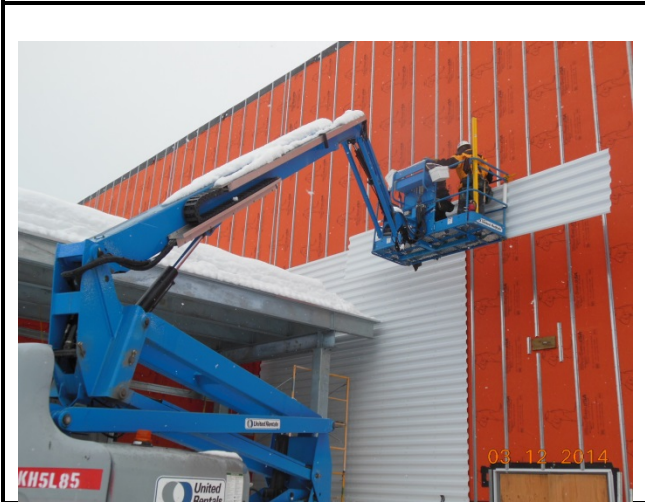

Installing MP-2 siding on Gym wall at CTE canopy



Dust collector drops attached to plywood walls in CTE



Sliding boiler unit through door to Mechanical Room



Boilers set on housekeeping pads in Mechanical Room



Data cable in trays above ceiling in classroom area



Close-up of cable bundles in tray suspended from structure

VALDEZ MIDDLE SCHOOL
CONSTRUCTION PHOTO REPORT No. 14- 10
MARCH 10, 2014 -MARCH 16, 2014



Terminating Admin area power circuits at panel "LR-3"



Wires neat and terminated in panel LR-3



Service disconnect gear (left) and panels in Electrical Rm



Spraying paint on walls followed by rolling (typical process)



Exterior metal doors painted and drying in Fitness room



Spraying "dry fall" paint on Gym trusses, duct and ceiling
