

# VALDEZ MIDDLE SCHOOL

## CONSTRUCTION PHOTO REPORT No. 14 - 13

### MARCH 31, 2014 -APRIL 6, 2014

#### KEY CONSTRUCTION ACTIVITIES

Dawson continued installing metal siding and flashing on the north and east walls. Inside, Dawson continued preparing floors for tile, started installing athletic equipment in the Gym, installed plywood on Shipping & Receiving walls and performed other rough carpentry as needed. Megawatt continued pulling wire for controls, installed lighting fixtures in CTE and the Gym and trimmed wall receptacles at classrooms. Integrity pulled data cable at Admin, Commons, the Gym and CTE areas, assembled equipment racks in upper (main) Comm. room, and pulled "backbone" cables from upper to lower Comm. room. Mantech installed fuel piping; seismic restraints and smoke sealed pipe penetrations in the Boiler room, installed piping to air movers in the Penthouse, and started installing sinks, fountains and toilets. All Wall finished hanging GWB in the Mechanical stairwell; continued sound caulking, continued taping and sanding the west side, Mechanical stairwell and Mat room; finished painting NW area classrooms and started installing ceiling grid in classrooms. Commercial Contractors continued preparing floors, installing and grouting ceramic floor and wall tile in toilet, locker and shower areas. Harris Sand & Gravel removed snow and ice around the building's west and north sides. This will help thaw the ground prior to excavation for the water line and permanent utilities.



Attaching metal siding (at left) on hat channels along north side of Mat room, Fitness and Mechanical areas (DCI image)

**VALDEZ MIDDLE SCHOOL**  
**CONSTRUCTION PHOTO REPORT No. 14 - 13**  
**MARCH 31, 2014 -APRIL 6, 2014**




Removing snow and ice along water line route



Installing piping for air moving equipment in Penthouse



Installing backstops, mat hoists and lights in the Gym

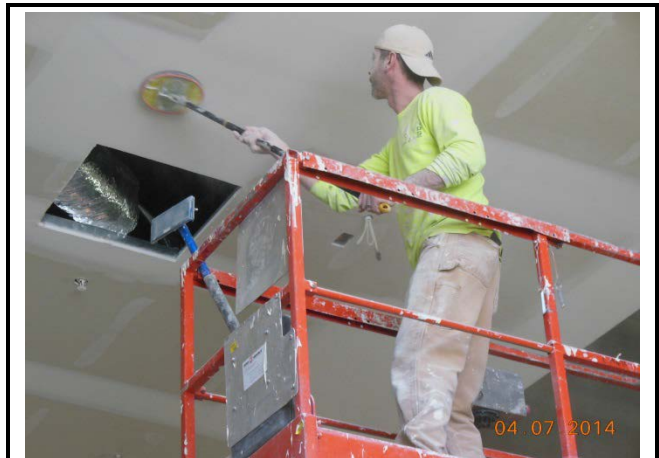

Final sanding sheetrock ceiling in the Mat room



Starting grid for acoustical ceiling tile in classroom



Grid finished and light fixtures installed in classroom

**VALDEZ MIDDLE SCHOOL**  
**CONSTRUCTION PHOTO REPORT No. 14 - 13**  
**MARCH 31, 2014 -APRIL 6, 2014**



Installing casework in 7<sup>th</sup> Grade classrooms




Installing casework below Science windows (DCI image)



Pulling data cable in the Admin area



Grouting ceramic wall tile in Toilet room

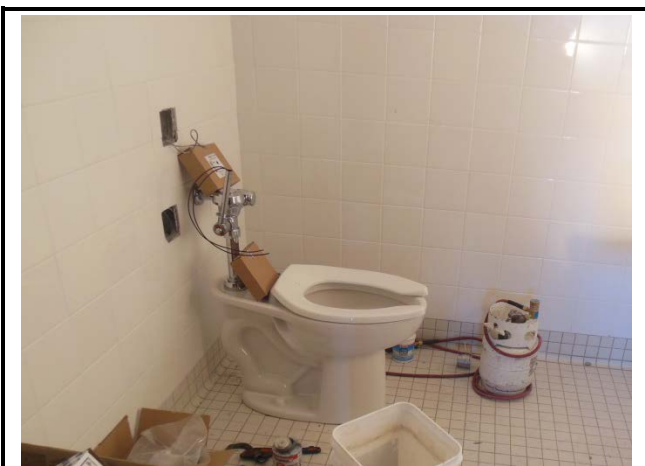

Starting to install bathroom toilet fixtures



Installing stainless steel sink in CTE area
