

VALDEZ MIDDLE SCHOOL
CONSTRUCTION PHOTO REPORT No. 14 – 23
JUNE 9, 2014 – JUNE 15, 2014

KEY CONSTRUCTION ACTIVITIES

Dawson worked on siding and started soffit under covered walkway; placed insulation for slab under HS canopy; installed bollards, concrete curb, sidewalks and dumpster pad; finished construction of seat wall next to HS; started forming foundations for goal posts and drains at athletic field; and moved field trailers to south side of site. Harris S&G finished flushing and testing water lines; continued subgrade prep and started installing drainage for athletic field and track; prepared subgrade for curb, sidewalk and site improvements; and backfilled seat wall next to HS. Inside, Dawson installed lockers, wood doors and marker boards; cleaned floors; helped subcontractors move materials; and erected steel for climbing wall. Megawatt continued installing light fixtures; continued installing conduit and wire and erected light poles; energized permanent power and turned on lights. ATS started trim for low voltage systems and worked on sound systems. Integrity started work on data systems. Mantech installed radiant tubing for HS covered walkway; completed fuel piping between the storage and boiler day tank; finished flushing water lines; and worked on fixtures and trim. H&H installed grills. All-Wall continued installing acoustical ceiling tile and wood slat ceiling at west-side commons. B&R Installations assembled the Gym bleachers. Door Systems of Alaska started installing roll up doors and operable partitions. CVEA turned on permanent power for high school and CVTC continued installing fiber and phone lines to both schools.



Subgrade prep for north end of running track and D-zone; layout and prep in progress for perimeter drainage system.

**VALDEZ MIDDLE SCHOOL
CONSTRUCTION PHOTO REPORT No. 14 – 23
JUNE 9, 2014 – JUNE 15, 2014**



CVEA conduit and conductor to new transformer for HS



CVEA transformer activated for MS



Finishing concrete slab for dumpsters



Protective collars were set and light poles were erected



Radiant heat tubing on rigid insulation for HS walkway



Compacting fill placed around seat wall near HS

**VALDEZ MIDDLE SCHOOL
CONSTRUCTION PHOTO REPORT No. 14 – 23
JUNE 9, 2014 – JUNE 15, 2014**




Installing sound system equipment in Reception area



Lights on and marker boards installed in classroom



Welding structural frame for climbing wall in Mat room

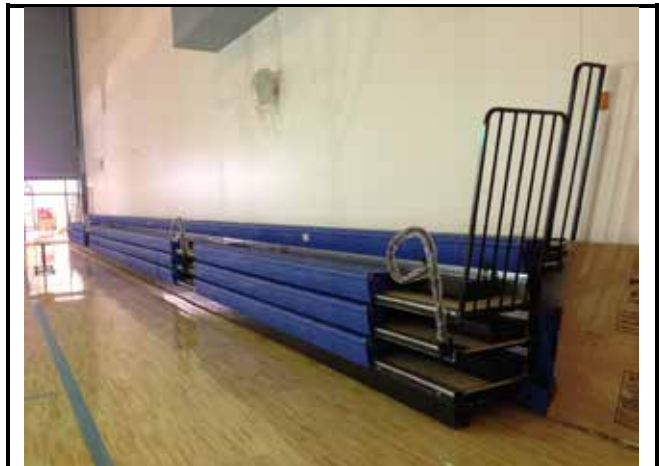

Gym bleachers installed (above at east wall)



Roll up doors were installed (above at CTE)



Lockers were installed; benches to follow
